

FIELD OBSERVATION REPORT



POSTL - YORE AND ASSOCIATES, INC.
2100 GOLF ROAD. ROLLING MEADOWS, IL. 60008

PROJECT: Dana Point - Balcony Rehabilitation PROJECT #: 10145.02 DATE: May 16, 2013

Work performed today:

AM Crew continues to install formwork at 1605-410B.

They were going to pour concrete tomorrow but spoke to P.D. Dick. Instead of making it on site, they will use ready mix trucked in and test.

Will start 1605-418C and pour both roof concrete the same day.

PM Crew has finished prepping 1605-410B for concrete. It is supposed to pour tomorrow.

Called Joe. Left Message to close up roof and to be here Monday morning to open up 418C.

Must notify 318C that their furniture may be moved around for wood supports.

Weather

Partially Cloudy

Temp.

AM

73

P.M.

Work force:

No.

Postl-Yore

Project Manager

Foreman

Laborer

LMS

Others

Maggie

Leo

Craig + Benny

Equipment:

Fork Lift
Boom Lift

1

1

Hrs.

Extra work:

Authorized by:

Approx. price

Material delivered to site:

Signature of

Architectural Representative:

MP

Report No.:


220

Copies: Lisette Ray, CMCA



1605-41013 (CAM)

5/16/13

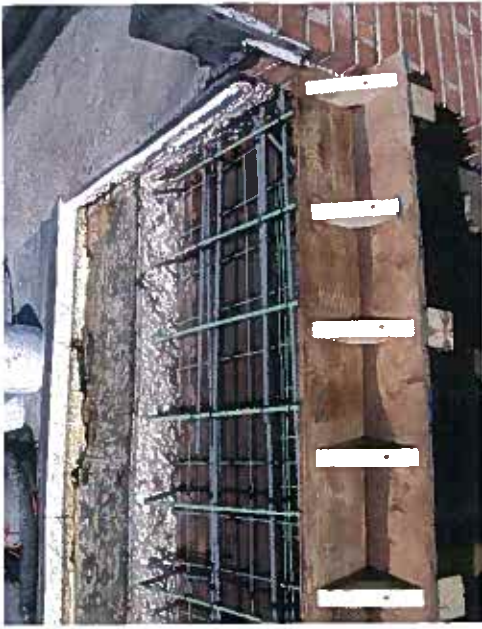

1605-410B (CPM)





11005-410 B





1605-418C
