

# FIELD OBSERVATION REPORT



POSTL - YORE AND ASSOCIATES, INC.  
2100 GOLF ROAD. ROLLING MEADOWS, IL. 60008

PROJECT: Dana Point - Balcony Rehabilitation


PROJECT #: 10145.02

DATE: June 18, 2013

<b>Work performed today:</b> Crew working on warranty issues for 1615 106A - Not done 1615 - 402A - Not done 1615 - 421 1/2 C - Not done 1615 - 222 C - Done 1605 - 313 B - Done			Weather <u>Overcast</u> Temp. AM <u>    </u> P.M. <u>72</u>																															
Crew was washing stain off of 200A. Unit owner said they stained it. Told Leo they should have called me. Washing it released up finish at 106A before. Back-pitched repairs still wet. Benny will be here tomorrow to finish the 3 not done. DM added new warranty balcony 1605-402A. Rick said it will take 3 days. They will start on Monday June 24, 2013.			Work force: No. Postl-Yore Project Manager <u>Maggie</u> Foreman <u>Leo</u> Laborer <u>Cruz Benny</u> LMS <u>    </u> Others <u>    </u>																															
			Equipment: <table border="1"> <thead> <tr> <th></th> <th></th> <th>Hrs.</th> </tr> </thead> <tbody> <tr> <td>Fork Lift</td> <td>1</td> <td></td> </tr> <tr> <td>Boom Lift</td> <td>1</td> <td></td> </tr> <tr><td> </td><td> </td><td> </td></tr> <tr><td> </td><td> </td><td> </td></tr> <tr><td> </td><td> </td><td> </td></tr> <tr><td> </td><td> </td><td> </td></tr> <tr><td> </td><td> </td><td> </td></tr> <tr><td> </td><td> </td><td> </td></tr> <tr><td> </td><td> </td><td> </td></tr> </tbody> </table>				Hrs.	Fork Lift	1		Boom Lift	1																						
		Hrs.																																
Fork Lift	1																																	
Boom Lift	1																																	
Extra work:	Authorized by:	Approx. price	Material delivered to site:																															
Signature of Architectural Representative: <u>MP</u>			Report No.: <u>243</u>																															
Copies: Lisette Ray, CMCA																																		



1615-222c

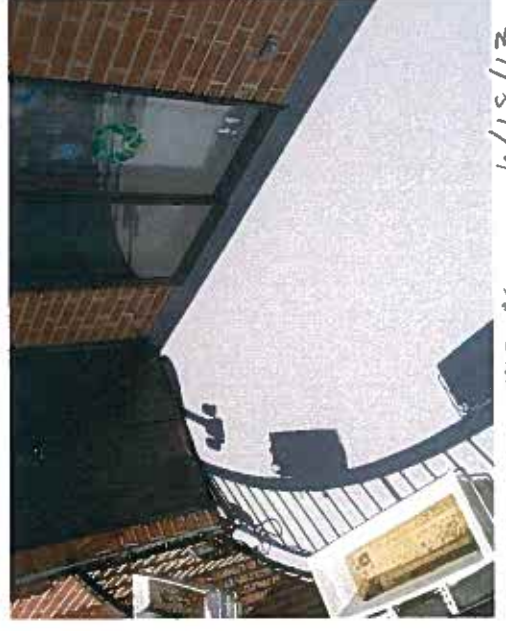

402A

6/18/13



402A



402A



402A



402A



402A



1615-402A





313B



313B



1605-313B



106A
