

FIELD OBSERVATION REPORT



POSTL - YORE AND ASSOCIATES, INC.
2100 GOLF ROAD, ROLLING MEADOWS, IL. 60008

PROJECT: Dana Point - Balcony Rehabilitation

PROJECT #: 10145.02

DATE: June 12, 2013

Work performed today:		Weather	Overcast/Partly Sunny
Peterson crew working on both roofs 1605-418C & 1605-411B.		Temp. AM	69 P.M.
Bucket has been removed at 1605-304A		Work force:	No.
Quality crew still working on membranes. Normal brown paint alongside to finish up ceiling areas for punchlisting.		Postl-Yore	Maggie
They will try to finish everything by Friday.		Project Manager	
Juan - D.P. Maintenance said there was membrane damage when he removed the door. The membrane will need to be fixed up.		Foreman	Lee
		Laborer	Craig + Bevay
		LMS	Peterson Roofers
		Others	+ 6
		Equipment:	Hrs.
		Forc lift	1
		Boom lift	1
Extra work:		Authorized by:	Material delivered to site:
Signature of Architectural Representative: <i>MR</i>		Report No.: 239	
Copies: Lisette Ray, CMCA			



1605-307A



1605-418C
6/12/13




1605-410B



1605-418C



1605 - 30714

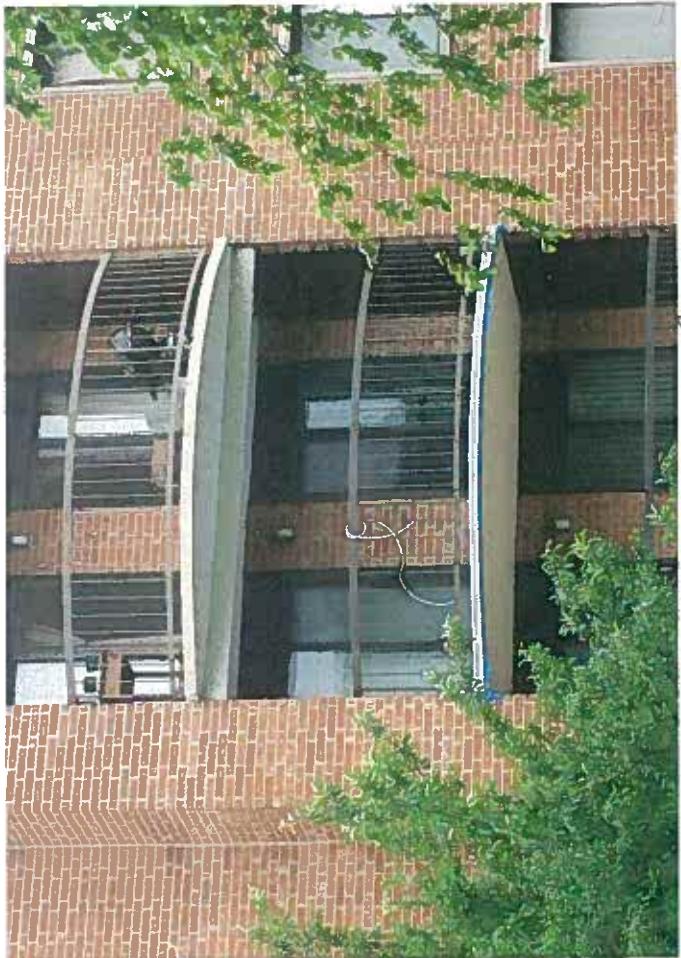

1605-304 A



411 B



1415-411 B
