

FIELD OBSERVATION REPORT




POSTL - YORE AND ASSOCIATES, INC.
2100 GOLF ROAD. ROLLING MEADOWS, IL. 60008


PROJECT: Dana Point - Balcony Rehabilitation

PROJECT #: 10145.02

DATE: June 3, 2013

| | | | |
|--|--------------------|------------------|-----------------------------|
| Work performed today: | | Weather | Sunny |
| <i>Roof repair @ 1415-411B is prepped, primed, and ready for concrete.</i> | | Temp. AM | <u>65</u> P.M. |
| Scheduled to arrive between 11-11:30 am. | | Work force: | No. |
| <i>Meeting @ 10:30 w/ 1415-415B and owner to observe conditions of that ceiling.</i> | | Postl-Yore | <i>Marcie</i> |
| <i>Rain last week delayed concrete pour so membranes will not be starting today.</i> | | Project Manager | <i>Off</i> |
| <i>Crew will take down forms from 1605-410B & 418C today as well.</i> | | Foreman | <i>Joe</i> |
| <i>Prop ceilings so that roofers can close them up on Wednesday.</i> | | Laborer | <i>Crug Benny Jim</i> |
| <i>Roofers will come at end of day to temporarily close 415-411B.</i> | | LMS | <i>Off</i> |
| | | Others | <i>Truck Driver</i> |
| | | Equipment: | Hrs. |
| | | <i>Boom lift</i> | <i>1</i> |
| | | <i>Fork lift</i> | <i>1</i> |
| Extra work: | Authorized by: | Approx. price | Material delivered to site: |
| | | | <i>Concrete</i> |
| Signature of Architectural Representative: | <i>[Signature]</i> | | Report No. : <i>232</i> |
| Copies: Lisette Ray, CMCA | | | |

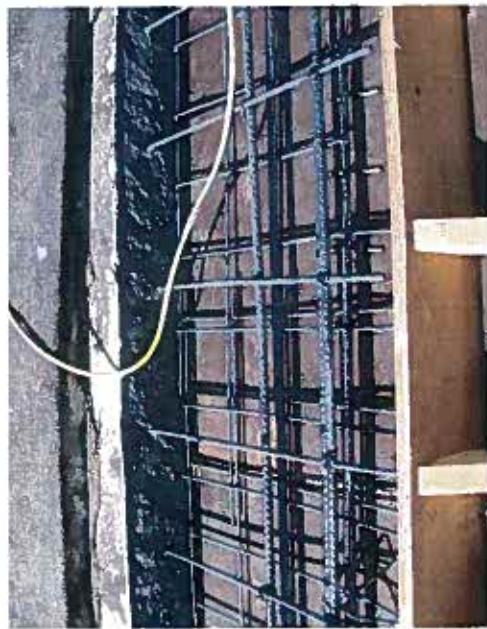



11/15-415PM






256B



256B

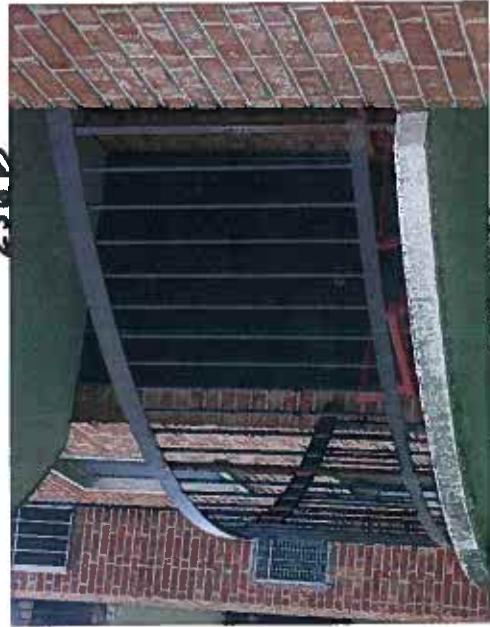

185-256B



411B



411B



411B



185-411B
